

LOCATION 1303 Fairfield Dr.CITY Los AngelesBETWEEN CarltonSTREET & Clinton

STREET


	SIZE	TYPE	LENGTH	INSTALLED	RETIRED	RENEWED
MAIN TO BLDG.	<u>3/4</u>	<u>Plastic</u>	<u>152</u>	<u>8-3-94</u>		
MAIN TO PROP. LINE	<u>3/4</u>	<u>"</u>	<u>46</u>			
PROP. LINE TO BLDG.	<u>3/4</u>	<u>"</u>	<u>106</u>			

ENTERS: 1303

BRANCHED INTO:

TAP SIZE: 1/2 PRESSURE _____ P.S.I. _____ INCHES W.C. LOCATION W side of housePRESSURE TEST: @ 100 psi For 44 Hrs. By BennettMAIN-SIZE 2 C.I. _____ BARE STEEL _____ COATED STEEL _____ PLASTIC — YEAR INSTALLED 1989DEPTH: 2 Ft. 6 In. LOCATION 16' N of C. Alt"A" P/S READING _____ TOTAL ANODES 1* _____ 17* _____ L.R. # 00336874

REMARKS:

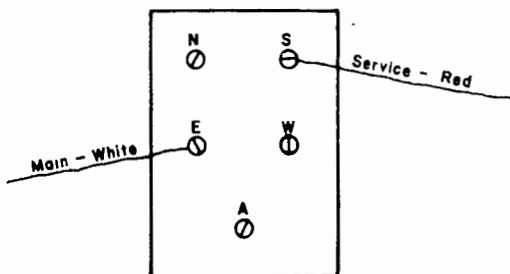

Test Station		
Reading & Location	Lead	Volts
P/S Pipeline Lead - Red New Service	S	
P/S Pipeline Lead - White Existing Main	E	

ENG. DEPT. USE ONLY
