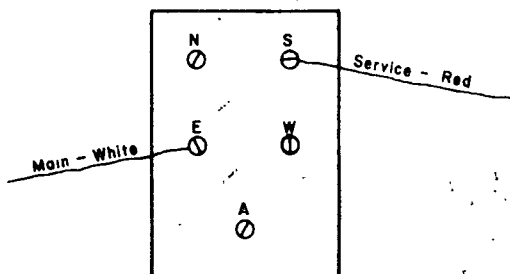


LOCATION 3763 Kennedy Rd.CITY GASTON IABETWEEN End of Caldesack.STREET & Kendrick Rd.

STREET

	SIZE	TYPE	LENGTH	INSTALLED	RETIRED	RENEWED
MAIN TO BLDG.	<u>3/4</u>	<u>Plastic</u>	<u>135'</u>	<u>8-22-94</u>		
MAIN TO PROP. LINE	<u>3/4</u>	<u>Plastic</u>	<u>45'</u>			
PROP. LINE TO BLDG.	<u>3/4</u>	<u>Plastic</u>	<u>90'</u>			

ENTERS:

BRANCHED INTO: 0TAP SIZE: 1/2 PRESSURE 60 P.S.I. _____ INCHES W.C. LOCATION 413' S of C of Newcomb LanePRESSURE TEST: @ 100 psi For 1/4 Hrs. By RLMAIN-SIZE 2" C.I. _____ BARE STEEL _____ COATED STEEL _____ PLASTIC ☒ YEAR INSTALLED 1993DEPTH: 3 Ft. 0 In. LOCATION 19' E of C of Kennedy Rd."A" P/S READING Plastic TOTAL ANODES 1# _____ 17# _____ L.R. # _____REMARKS: New 3/4 Plastic Service, with Road Bore.

Test Station		
Reading & Location	Lead	Volts
P/S Pipeline Lead - Red New Service	S	Riser Plastic
P/S Pipeline Lead - White Existing Main	E	

ENG. DEPT. USE ONLY
